

Amend Recreation Center: Weekly Update 10-3-2025

VP-Eastern District: Jason Hubbard jhub@langlas.com

Project Manager: Rachel Guisti rachelb@langlas.com

SR. Project Superintendent: Lane Huffman <u>lhuffman@langlas.com</u>

Field Engineer: Si Ryan <u>sir@langlas.com</u>

Progress Summary: Week of September 29th

Langlas:

Layout Light Poles

Layout Interior Walls

Pressure Wash all Trusses and Columns for the Painters

Billings Concrete:

Pour Mechanical Slabs on the North

Weave:

Start to cut subgrade in the South Parking lots

J & B Erectors: (True North)

Building Trusses

Started to Install Gym Equipment Beams

• Central Electric:

Trenching for light poles Running Conduit in Trusses


Painters Inc.:

Pre-Painting Trusses while on the ground







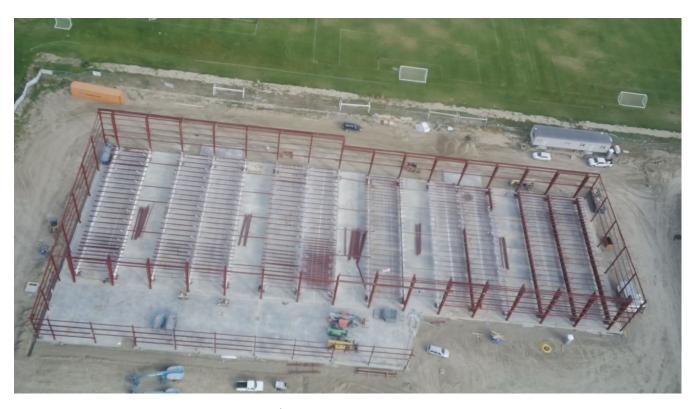

Schedule: Upcoming week of October 6th

• Langlas:

Laying out-Gym Openings Setting Door Frames Review Submittals Material Take Off

Weave:

Parking Lot Gravel on the South
Prepping for Concrete guys to start curb and gutter

• Plumb MT:

Exterior Gas Lines around the north side

Central Electric:

Rough-in Trusses Site Light Poles

J & B Erectors

Continue trusses and prepping for erection

Painters Inc.:

Painting Trusses and Columns
